



Date: 2/5/25

Nevada Department of Transportation (NDOT)

Stormwater Pollution Prevention Plan
(SWPPP) Template for Construction
Activities



Table of Contents

Page #

STORM WATER POLLUTION PREVENTION SITE INFORMATION	3
STORM WATER POLLUTION PREVENTION TEAM	5
PROJECT DESCRIPTION & NATURE OF CONSTRUCTION ACTIVITIES	7
EMERGENCY-RELATED CONSTRUCTION ACTIVITIES	8
SEQUENCE AND ESTIMATED DATES OF CONSTRUCTION ACTIVITIES	9
EXISTING SOIL CHARACTERISTICS	11
SITE MAPS	13
RECEIVING WATERS	14
SEDIMENT AND EROSION CONTROLS	15
SUMMARY OF POTENTIAL POLLUTANT SOURCES	17
SPILL PREVENTION AND RESPONSE	19
MATERIALS STORAGE, SPILL PREVENTION AND RESPONSE	19
INSPECTION/MAINTENANCE PROCEDURES	23
1. INSPECTION PROCEDURES	23
2. INSPECTION DOCUMENTATION	24
3. MAINTENANCE PROCEDURES	24
4. CORRECTIVE ACTION PROCEDURES	24
ADDITIONAL INFORMATION	25
1. CONTROL MEASURE ADDITION/REPAIR/MODIFICATION	25
2. DEPARTURES FROM DESIGN SPECIFICATIONS	25
3. CULVERT STABILIZATION	26
4. SPECIAL CONSTRUCTION DISTURBANCES	26
5. LINEAR CONSTRUCTION PROJECTS	26
a. TRACK-OUT (LINEAR CONSTRUCTION PROJECTS)	27
6. SEDIMENT OR STOCKPILES	27
7. NON-VEGETATIVE FINAL STABILIZATION METHODS	27
8. DISCHARGES TO IMPAIRED WATERBODIES WITHOUT ESTABLISHED TOTAL MAXIMUM DAILY LOADS	27
9. DISCHARGES TO IMPAIRED WATERBODIES WITH ESTABLISHED TOTAL MAXIMUM DAILY LOADS	28
10. SEDIMENT BASIN DISCHARGES	28
11. ADDITIONAL DISCHARGE REQUIREMENTS	29
DOCUMENTATION REQUIREMENTS	30
1. NOTICE OF INTENT (NOI)	30
2. APPROVAL LETTER	30
3. PERMIT	30
4. SIGNIFICANT SPILLS/LEAKS/RELEASES	30
5. STRUCTURAL CONTROL MEASURE REPAIRS	30
6. INSPECTION REPORTS	30
7. CORRECTIVE ACTION	30
8. BUFFER DOCUMENTATION	31
9. EMPLOYEE TRAINING RECORDS/CERTIFICATIONS	31
10. PLANS REQUIRED BY OTHER AGENCIES	31
11. DEMINIMIS DISCHARGES	31

DOCUMENTATION OF COMPLIANCE WITH <u>EPA CGP REQUIRED PERMITTED</u>	
<u>SITES (Tribal Lands)</u>	31
1. ENDANGERED SPECIES PROTECTION.....	31
2. HISTORIC PRESERVATION	31
3. SAFE DRINKING WATER ACT UNDERGROUND INJECTION CONTROL REQUIREMENTS	31
CERTIFICATIONS OF COMPLIANCE	31
1. OWNER/OPERATOR CERTIFICATION STATEMENT	32
2. CONTRACTOR'S CERTIFICATION STATEMENT	33
ATTACHMENT A	34
SITE MAP.....	35
SITE PROFILES.....	36
TOPO MAP	37
DISTURBED AREAS, SURROUNDING WATERS MAP	38
INSPECTION FORM.....	39
ATTACHMENT B	40

Disclaimer:

This template is designed to provide guidance through the SWPPP development process and help to ensure the SWPPP addresses all the necessary elements stated in the applicable construction general permit and the requirements of NDOT. It is the responsibility of the Operator to include the correct and proper information, understand the NDEP and/or EPA Construction General Permit requirements, and create a document that meets regulatory compliance.

STORM WATER POLLUTION PREVENTION SITE INFORMATION

PROVIDE SITE, OWNER, OPERATOR AND ADDITIONAL OPERATORS INFORMATION. The SWPPP must include a list of all operators who will be engaged in construction activities at your site, and the areas over which they have control.

Site Description Information:	
NDOT Contract # (If the project does not have an NDOT Contract # provide a project #)	4529
NDEP Permit CSW # and /or EPA Permit Tracking #	CSW-55080 and 55209
Project Name	NDOT 4529 Eureka County
Address Line #1 (If the address is not applicable then provide route and milepost)	I-80 MP EU 4.120 to 4.950
Address Line #2	
City	Dunphy
State	Nevada
County	Eureka
Assessor's Parcel Number (APN#)	near 422009

Owner Information:	
Name	Nevada Division of Transportation
Address Line #1	1263 South Stewart Street
Address Line #2	
City	Carson City
State	Nevada
Zip Code	89712
Contact Name	David Knight
Phone Number	7754314672
Email Address	dknight@dot.nv.gov

Operator Information:	
Name	Q&D Construction LLC
Address Line #1	1050 South 21st Street
Address Line #2	
City	Sparks
State	Nevada
Zip Code	89431
Contact Name	Temo Licea
Phone Number	7553995207
Email Address	tllicea@qdconstruction.com
If there is more than one operator, identify the areas and/or phases over which the designated operator has control	

Additional Operator #2 Information:	
Name	
Address Line #1	
Address Line #2	
City	
State	
Zip Code	
Contact Name	
Phone Number	
Email Address	
If there is more than one operator, identify the areas and/or phases over which the designated operator has control	

Additional Operator #3 Information:	
Name	
Address Line #1	
Address Line #2	
City	
State	
Zip Code	
Contact Name	
Phone Number	
Email Address	
If there is more than one operator, identify the areas and/or phases over which the designated operator has control	

Notice of Intent (NOI):	
Filing Date	2/6/25
Approval Date	2/10/25

NOTE: A WORKING COPY OF THIS SWPPP MUST BE KEPT AT THE CONSTRUCTION SITE OR BE LOCALLY AVAILABLE FOR REVIEW BY NDEP, EPA AND LOCAL REGULATORY AGENCIES.

A COPY OF THE NDEP CONSTRUCTION STORMWATER GENERAL PERMIT NVR100000 AND/OR FEDERAL (CGP) STORMWATER CONSTRUCTION GENERAL PERMIT NVR120001 AND THE NOTICE OF INTENT FOR THIS PROJECT MUST BE ATTACHED TO THIS SWPPP AS APPROPRIATE. GUIDANCE FOR SELECTING AND IMPLEMENTING BMPs IS AVAILABLE IN THE NEVADA DEPARTMENT OF TRANSPORTATION CONSTRUCTION SITE BEST MANAGEMENT PRACTICES (BMPs) MANUAL.

<http://www.nevadadot.com/StormWater/Resources.aspx>

ATTACH ADDITIONAL PAGES WHEN NECESSARY TO PROVIDE THE REQUIRED INFORMATION.

STORM WATER POLLUTION PREVENTION TEAM

LIST THE NAME, TITLE, EMPLOYER, AND INDIVIDUAL RESPONSIBILITIES FOR EACH MEMBER OF THE STORMWATER TEAM. THE STORMWATER TEAM IS RESPONSIBLE FOR OVERSEEING THE INITIAL DEVELOPMENT OF THE SWPPP, ANY MODIFICATIONS TO THE SWPPP, UPDATING THE SWPPP AS NECESSARY, AND COMPLIANCE WITH THE REQUIREMENTS OF THE **NDEP CONSTRUCTION STORMWATER GENERAL PERMIT NVR100000 AND/OR FEDERAL (CGP) STORMWATER CONSTRUCTION GENERAL PERMIT NVR 120001**. THE TEAM MAY INCLUDE MEMBERS THAT ARE NOT EMPLOYED BY THE OPERATOR (I.E. *THIRD PARTY CONSULTANTS*). FOR NDOT CONTRACTS, PROVIDE THE NAME OF THE WATER POLLUTION CONTROL MANAGER AND INCLUDE 24 HOUR CONTACT INFORMATION.

Stormwater Team Member #1 Information:

Name	Scott Leone
Title	Project Superintendent
Phone Number	7753026540
Responsibilities	Oversight of the foreman to ensure SWPPP measures and construction activities are being properly executed.

Stormwater Team Member #2 Information:

Name	Temo Licea
Title	Project Manager
Phone Number	7753995207
Responsibilities	Responsible for coordination between Q&D and any subcontractors that may be necessary

Stormwater Team Member #3 Information:

Name	James McCain
Title	Safety Director
Phone Number	7753537103
Responsibilities	Responsible for ensuring all workers are taking the necessary precautions and performing their duties in a safe and responsible manner on the job site.

Stormwater Team Member #4 Information:	
Name	TBD
Title	Foreman
Phone Number	
Responsibilities	Responsible for ensuring all workers are taking the necessary precautions and performing their duties in a safe and responsible manner on the job site.
Stormwater Team Member #5 Information:	
Name	Gracie Damele
Title	Environmental Compliance Engineer/WPCM
Phone Number	7753026407
Responsibilities	Oversight of the foreman to make sure SWPPP measures and construction activities are being properly executed.

ATTACH ADDITIONAL PAGES WHEN NECESSARY TO PROVIDE THE REQUIRED INFORMATION.

PROJECT DESCRIPTION & NATURE OF CONSTRUCTION ACTIVITIES

DESCRIBE THE NATURE OF THE CONSTRUCTION ACTIVITIES, INCLUDING THE SIZE OF THE PROPERTY(IES) AND THE LOCAL AREA(S) EXPECTED TO BE DISTURBED BY CONSTRUCTION ACTIVITIES, CONSTRUCTION SUPPORT ACTIVITY AREAS COVERED BY THE PERMIT (I.E. STAGING AREAS AND LAYDOWN AREAS), AND THE MAXIMUM AREA EXPECTED TO BE DISTURBED AT ANY ONE POINT IN TIME. DESCRIBE THE INTENDED USE AFTER THE NOTICE OF TERMINATION (E.G. HIGHWAY, LOW DENSITY COMMERCIAL).

DESCRIPTION OF THE PROPOSED CONSTRUCTION ACTIVITY:

Mill bridge deck, concrete delamination, apply polymer bridge deck

INTENDED SEQUENCE OF MAJOR SOIL DISTURBING ACTIVITIES

see attached schedule, no major soil disturbing activities

TOTAL AREA OF SITE (ACRES)	TOTAL AREA EXPECTED TO BE DISTURBED BY CONSTRUCTION ACTIVITIES (ACRES)	MAXIMUM AREA EXPECTED TO BE DISTURBED BY CONSTRUCTION ACTIVITIES AT ANY ONE TIME (ACRES)
10	8.4	9.7

EMERGENCY-RELATED CONSTRUCTION ACTIVITIES

FOR EARTH-DISTURBING ACTIVITIES IN RESPONSE TO A PUBLIC EMERGENCY, DOCUMENT THE CAUSE OF THE PUBLIC EMERGENCY, PROVIDE INFORMATION SUBSTANTIATING ITS OCCURRENCE, AND DESCRIBE THE CONSTRUCTION NECESSARY TO RE-ESTABLISH AFFECTED PUBLIC SERVICES.

CAUSE OF THE PUBLIC EMERGENCY:

DESCRIBE THE CAUSE OF THE PUBLIC EMERGENCY (E.G. NATURAL DISASTER, EXTREME FLOODING CONDITIONS, ETC.)

N/A

SUBSTANTIATING INFORMATION

PROVIDE INFORMATION SUBSTANTIATING THE OCCURRENCE OF THE PUBLIC EMERGENCY (SUCH AS A STATE DISASTER DECLARATION OR SIMILAR DECLARATION). ATTACH SUPPORTING DOCUMENTATION TO THE END OF THE SWPPP.

N/A

NECESSARY CONSTRUCTION

DESCRIBE THE NECESSARY CONSTRUCTION TO RE-ESTABLISH AFFECTED PUBLIC SERVICES.

N/A

SEQUENCE AND ESTIMATED DATES OF CONSTRUCTION ACTIVITIES

PROVIDE A SCHEDULE OF THE ESTIMATED START DATES AND THE DURATION OF THE ACTIVITY FOR INSTALLATION OF STORMWATER CONTROL MEASURES, CONSTRUCTION ACTIVITIES, CESSATION OF THE CONSTRUCTION ACTIVITIES, AND STABILIZATION OF AREAS OF EXPOSED SOIL.

INSTALLATION OF STORMWATER CONTROL MEASURES

WHAT IS THE ESTIMATED START DATE FOR THE INSTALLATION OF STORMWATER CONTROL MEASURES?

3/3/25

WHAT IS THE ESTIMATED DURATION OF THE INSTALLATION OF STORMWATER CONTROL MEASURES? (CALENDAR DAYS)

1 Day

WHAT DATE WILL THE STORMWATER CONTROL MEASURES BE MADE OPERATIONAL?

3/3/25

SEQUENCE:

See attached schedule

CONSTRUCTION ACTIVITIES

WHAT IS THE ESTIMATED START DATE OF CONSTRUCTION ACTIVITIES?

3/3/25

WHAT IS THE ESTIMATED DURATION OF CONSTRUCTION ACTIVITIES? (CALENDAR DAYS)

50 Working Days

DESCRIBE THE INTENDED SEQUENCE OF CONSTRUCTION ACTIVITIES. IF ADDITIONAL SPACE IS NEEDED ADD AS APPENDIX.

See attached schedule

CESSATION OF CONSTRUCTION ACTIVITIES			
WHAT IS THE ESTIMATED DATE FOR THE CESSATION OF CONSTRUCTION ACTIVITIES?	5/9/25		
WILL THE CESSATION OF CONSTRUCTION ACTIVITIES BE TEMPORARY OR PERMANENT?	☐	TEMPORARY	☒ PERMANENT
IF THE CESSATION OF CONSTRUCTION WILL BE TEMPORARY, PROVIDE THE ESTIMATED DURATION OF THE CESSATION OF THE CONSTRUCTION ACTIVITIES. (CALENDAR DAYS)	N/A		
WILL THE CESSATION OF CONSTRUCTION ACTIVITIES OCCUR ON THE ENTIRE SITE (100%) OR IN DESIGNATED PORTIONS OF THE SITE? WILL IT BE TEMPORARY OR PERMANENT?	100%		☐ DESIGNATED PORTIONS
IF THE CESSATION OF CONSTRUCTION ACTIVITIES WILL OCCUR ONLY IN DESIGNATED PORTIONS OF THE SITE, IDENTIFY THE DESIGNATED PORTIONS OF THE SITE WHERE THE CESSATION OF CONSTRUCTION ACTIVITIES WILL OCCUR.			
N/A			
STABILIZATION OF AREAS OF EXPOSED SOIL			
WHAT IS THE ESTIMATED START DATE FOR THE TEMPORARY STABILIZATION OF AREAS OF EXPOSED SOIL?	no exposed soil		
WHAT IS THE ESTIMATED DURATION OF THE TEMPORARY STABILIZATION OF AREAS OF EXPOSED SOIL? (CALENDAR DAYS)			
WHAT IS THE ESTIMATED START DATE FOR THE FINAL STABILIZATION OF AREAS OF EXPOSED SOIL?			
WHAT IS THE ESTIMATED DURATION OF THE FINAL STABILIZATION OF AREAS OF EXPOSED SOIL? (CALENDAR DAYS)			
NOTE: THE DATES FOR STABILIZATION SHALL REFLECT THE APPLICABLE DEADLINES IN THE APPROPRIATE EPA/NDEP CONSTRUCTION GENERAL PERMIT REFERRING TO <u>STABILIZATION REQUIREMENTS, SCHEDULES, AND DEADLINES</u>.			

DEPARTURES FROM INITIAL PROJECTIONS
IF DEPARTURES FROM THE INITIAL PROJECTIONS FOR ANY OF THE ACTIVITIES NOTED ABOVE OF THIS SWPPP ARE NECESSARY, IDENTIFY AND DESCRIBE SUCH DEPARTURES. ALTERNATIVELY, DOCUMENTATION DESCRIBING SUCH DEPARTURES MAY BE ATTACHED TO THE END OF THE SWPPP.
Will identify any departures from the site if need be

EXISTING SOIL CHARACTERISTICS

PROVIDE A NARRATIVE DESCRIPTION OF THE EXISTING SITE SOIL CHARACTERISTICS (**SAND SOILS**: DRY, NUTRIENT DEFICIENT, FAST DRAINING. **SILT SOILS**: CRUST FORMING, DECREASED INFILTRATION IF OVERTILLED AND COMPACTED. **CLAY SOILS**: PERCENT CLAY DETERMINES ABILITY TO TRANSPORT WATER. **LOAM SOILS**: A COMBINATION OF SOIL TYPES IN VARYING DEGREES. <http://websoilsurvey.nrcs.usda.gov/app/> IDENTIFY THE EROSION POTENTIAL OF THE SOILS ON SITE. DESCRIBE THE PROCESS USED TO DETERMINE THE EROSION POTENTIAL OF THE SITE SOILS, AND DISCUSS HOW THE EROSION POTENTIAL INFLUENCED BMP SELECTION AND PLACEMENT. http://bettersoils.soilwater.com.au/module5/5_11.htm

N/A, No soil disturbance.

WHAT PERCENTAGE OF THE SITE IS IMPERVIOUS BEFORE AND AFTER CONSTRUCTION?

BEFORE %

10

AFTER %

10

FOR AREAS WHERE IT IS REQUIRED BY THE PERMIT TO ESTABLISH A 50-FOOT BUFFER, BUT IT IS INFEASIBLE TO MAINTAIN A 50-FOOT NATURAL BUFFER, PROVIDE THE REASON WHY THE 50-FOOT BUFFER CANNOT BE MAINTAINED, IDENTIFY AND DESCRIBE THE ALTERNATIVE ADDITIONAL EROSION AND SEDIMENT CONTROLS THAT WERE SELECTED FOR THE SITE, DOCUMENT THE NATURAL BUFFER WIDTH RETAINED ON THE PROPERTY, AND ATTACH ANY RELEVANT DOCUMENTATION TO THE END OF THE SWPPP.

NOTE: EPA DOES NOT CONSIDER STORMWATER CONTROL FEATURES (E.G., STORMWATER CONVEYANCE CHANNELS, STORM DRAIN INLETS, SEDIMENT BASINS) TO CONSTITUTE "SURFACE WATERS" FOR THE PURPOSE OF TRIGGERING THE REQUIREMENT TO COMPLY WITH THIS PART.

NOTE: AREAS THAT YOU DO NOT OWN OR THAT ARE OTHERWISE OUTSIDE YOUR OPERATIONAL CONTROL MAY BE CONSIDERED AREAS OF UNDISTURBED NATURAL BUFFER FOR PURPOSES OF COMPLIANCE WITH THIS PART.

N/A

IDENTIFY AND DESCRIBE ALL ON-SITE AND OFF-SITE MATERIALS STORAGE AREAS, INCLUDING OVERBURDEN, STOCKPILES OF DIRT, BORROW AREAS, ETC.

Off site staging area and material storage will take place at the Dunphy Rural Fire Station. Materials will have adequate BMPs in place including wattles/secondary containment if necessary.

SITE MAPS

1. ATTACH A GENERAL LOCATION MAP (1 mile radius of site) IN ATTACHMENT A.

2. ATTACH A DETAILED SITE MAP(s) IN ATTACHMENT A.

NOTE THAT SITE MAPS MUST BE UPDATED AND REVISED AS SITE CONDITIONS CHANGE AND NEW BMPS ARE IMPLEMENTED.

PROVIDE A CHECK MARK OR N/A AS APPROPRIATE IN THE FOLLOWING BOXES.

THE DETAILED SITE MAP CHECKLIST MUST INCLUDE THE FOLLOWING AS APPLICABLE:

YES N/A

- | | | |
|-------------------------------------|-------------------------------------|---|
| ☒ | ☐ | EXISTING AND PROPOSED TOPOGRAPHY AND DRAINAGE PATTERNS (INCLUDING FLOW ONTO, OVER AND FROM THE SITE) BOTH BEFORE AND AFTER MAJOR GRADING ACTIVITIES DRAWN TO SCALE WITH NORTH ARROW. INCLUDE EXISTING TYPES OF COVER (E.G. FOREST, PAVEMENT, STRUCTURES), ETC. |
| ☒ | ☐ | PROPERTY BOUNDARIES WITH THE PROJECT AREA CLEARLY IDENTIFIED. |
| ☒ | ☐ | LOCATIONS WHERE CONSTRUCTION ACTIVITIES WILL OCCUR, NOTING ANY APPLICABLE PHASING. SHOW AREAS OF SOIL DISTURBANCE AND AREAS THAT WILL NOT BE DISTURBED. |
| ☒ | ☐ | LOCATIONS WHERE SEDIMENT OR SOILS WILL BE STOCKPILED. |
| ☒ | ☐ | LOCATIONS OF ANY CROSSING OF SURFACE WATERS. |
| ☒ | ☐ | DESIGNATED POINTS ON THE SITE WHERE VEHICLES WILL EXIT ONTO PAVED ROADS. |
| ☐ | ☒ | LOCATIONS OF CONSTRUCTION SUPPORT ACTIVITY AREAS COVERED BY THE PERMIT (e.g. CONCRETE AND ASPHALT BATCH PLANTS). |
| ☒ | ☐ | LOCATIONS OF TEMPORARY AND PERMANENT STORMWATER CONTROL MEASURES IDENTIFIED IN THIS SWPPP. |
| ☐ | ☒ | LOCATIONS OF AREAS PROTECTED BY NATURAL BUFFERS INCLUDING THE BOUNDARY LINES OF ALL SUCH BUFFERS. |
| ☒ | ☐ | LOCATIONS OF STRUCTURAL AND NON-STRUCTURAL STORMWATER CONTROLS IDENTIFIED IN SWPPP. |
| ☒ | ☐ | LOCATIONS WHERE STABILIZATION CONTROL MEASURES AND PRACTICES ARE EXPECTED TO BE APPLIED. |
| ☒ | ☐ | LOCATIONS WHERE VEHICLES AND EQUIPMENT WILL BE STORED AND MAINTAINED. |
| ☐ | ☒ | LOCATIONS OF MATERIAL, BORROW, AND WASTE (INCLUDING CONCRETE WASHOUT AREAS). |
| ☒ | ☐ | LOCATION OF ALL POTENTIAL POLLUTANT-GENERATING ACTIVITIES IDENTIFIED IN THIS SWPPP. |
| ☒ | ☐ | LOCATIONS WHERE POLYMERS, FLOCCULANTS, OR OTHER TREATMENT CHEMICALS WILL BE USED AND STORED. |
| ☒ | ☐ | GENERAL LOCATION(S) AND AERIAL EXTENT OF ALL RECEIVING WATERS, WETLANDS AND THEIR TRIBUTARIES (INCLUDING IMPAIRED AND TMDL LISTED WATERS) WITHIN A 1 MILE RADIUS OF THE PROJECT AREA). |
| ☒ | ☐ | STORMWATER DISCHARGE LOCATIONS, USING ARROWS TO INDICATE DISCHARGE DIRECTIONS, INCLUDING: <ul style="list-style-type: none"> • LOCATION(S) WHERE STORMWATER AND/OR ALLOWABLE NON-STORMWATER DISCHARGES ARE DISCHARGED TO A WATER OF THE U.S. • LOCATION(S) OF ANY DISCHARGES TO MUNICIPAL SEPARATE STORM SEWER SYSTEMS (MS4S) |
| ☒ | ☐ | LOCATIONS OF ALL STEEP SLOPES. (PER EPA, THESE ARE DEFINED AS SLOPES THAT ARE 15% OR GREATER) |
| ☒ | ☐ | LOCATIONS WHERE FINAL STABILIZATION HAS BEEN ACCOMPLISHED AND NO FURTHER CONSTRUCTION PERMIT REQUIREMENTS APPLY. |
| ☐ | ☒ | LOCATION(S) OF TREES AND BOUNDARIES OF ENVIRONMENTALLY SENSITIVE AREAS AND BUFFER ZONES TO BE PRESERVED. |
| ☐ | ☒ | LOCATION(S) OF FEDERALLY LISTED CRITICAL HABITAT FOR ENDANGERED OR THREATENED SPECIES. |
| ☒ | ☐ | LOCATION(S) OF STRUCTURES AND OTHER IMPERVIOUS SURFACES UPON COMPLETION OF CONSTRUCTION. |
| ☒ | ☐ | LEGEND IDENTIFYING ALL SYMBOLS, BMP NUMBERS OR ABBREVIATIONS USED. |

RECEIVING WATERS

IDENTIFY THE NAME AND LOCATION OF ALL WATERWAYS (INCLUDING STREAMS, RIVERS, DITCHES, DRAINAGES, LAKES OR WETLANDS), AND OTHER SPECIAL AQUATIC SITES AT OR NEAR THE SITE THAT WILL RECEIVE DISCHARGE FROM THE CONSTRUCTION SITE. IF THE SITE WILL DRAIN TO THE MUNICIPAL STORM DRAIN SYSTEM (i.e., drop inlets, curbs, gutters, roadside ditches), IDENTIFY THE RECEIVING WATER TO WHICH THE MUNICIPAL STORM DRAIN SYSTEM DISCHARGES.

Humboldt River

IMPAIRED WATERS

IS ANY DISCHARGE POINT FROM THE CONSTRUCTION SITE WITHIN ¼ MILE OF AN IMPAIRED OR TMDL LISTED WATER?



YES



NO

IF ANY DISCHARGE POINT FROM THE CONSTRUCTION SITE IS WITHIN ¼ MILE OF AN IMPAIRED OR TMDL LISTED WATER, IDENTIFY ANY COMMON CONSTRUCTION-RELATED POLLUTANTS, SUCH AS SEDIMENT, SEDIMENT-RELATED PARAMETERS, AND NUTRIENTS (INCLUDING NITROGEN AND PHOSPHORUS), FOR WHICH THE IMPAIRED OR TMDL LISTED WATER IS IMPAIRED FOR THAT MAY POTENTIALLY BE DISCHARGED FROM THE CONSTRUCTION SITE, AND DESCRIBE ADDITIONAL OR ENHANCED CONTROL MEASURES TO MINIMIZE DISCHARGES OF THESE SPECIFIC POLLUTANTS. THE 303(D) LIST OF IMPAIRED WATERS AND TMDL LISTED WATERS CAN BE FOUND ON THE NEVADA DIVISION OF ENVIRONMENTAL PROTECTION (NDEP), BUREAU OF WATER QUALITY PLANNING (BWQP) WEBSITE. [HTTP://NDEP.NV.GOV/BWQP/303D_ARCHIVE.HTM](http://NDEP.NV.GOV/BWQP/303D_ARCHIVE.HTM)

Humboldt River from Palisade to Battle Mountain: Phosphorus, Total Suspended Solids. To reduce the possibility of further contamination in the event of sufficient rain to create runoff, fiber rolls may be used in an effort to slow and redirect the flow of runoff. Although runoff is highly unlikely for this type of project.

EROSION AND SEDIMENT CONTROLS

BEST MANAGEMENT PRACTICES (BMPS)

DESCRIBE EACH CONTROL MEASURE AND THE GENERAL SEQUENCE OF IMPLEMENTATION DURING THE CONSTRUCTION PROCESS. CLEARLY IDENTIFY BELOW THE BMPs THAT WILL BE USED FOR EACH OF THE MAJOR ACTIVITIES IDENTIFIED IN THE PROJECT DESCRIPTION & NATURE OF CONSTRUCTION ACTIVITIES ABOVE. ALSO INDICATE EACH OPERATOR THAT WILL BE RESPONSIBLE FOR INSTALLING AND MAINTAINING EACH CONTROL MEASURE.

NOTE: Under the NDEP CGP and EPA CGP, the use of cationic treatment chemicals are ineligible for coverage under the permit, unless the Permittee notifies the respective agency in advance and obtains written authorization for use.

CONTROL MEASURES	ACTIVITY/AREA	OPERATOR
Water truck to spray water as needed throughout grading and milling activities to reduce dust	project wide	Q&D
Sweeper may be a control measure to remove trackout on pavement	project wide/staging yard	Q&D
Straw wattles	project wide/staging yard	Q&D

CONTROL MEASURES	ACTIVITY/AREA	OPERATOR

SUMMARY OF POTENTIAL POLLUTANT SOURCES

POTENTIAL POLLUTANT SOURCES
IDENTIFY ALL POTENTIAL SOURCES OF POLLUTION THAT MAY REASONABLY BE EXPECTED TO AFFECT THE QUALITY OF STORMWATER DISCHARGES FROM THE CONSTRUCTION SITE. ALSO IDENTIFY THE LOCATION OF AND DESCRIBE ANY POLLUTANT SOURCES, INCLUDING ANY NON-STORMWATER DISCHARGES EXPECTED TO BE ASSOCIATED WITH THE PROJECT, FROM AREAS OTHER THAN CONSTRUCTION (I.E. SUPPORT ACTIVITIES INCLUDING STORMWATER DISCHARGES FROM DEDICATED ASPHALT OR CONCRETE PLANTS, AND ANY OTHER NON-CONSTRUCTION POLLUTANT SOURCES SUCH AS FUELING AND MAINTENANCE OPERATIONS, MATERIALS STORAGE ON-SITE, WASTE PILES, EQUIPMENT STAGING YARDS, ETC.).
POTENTIAL POLLUTANT SOURCE 1
WHAT IS THE LOCATION OF THE POTENTIAL POLLUTANT SOURCE? (e.g. ROUTE, MILEPOST, OR STATION)
Project wide.
DESCRIBE THE POTENTIAL POLLUTANT SOURCE AND ITS POLLUTANTS OF CONCERN.
Fluid leaks from equipment (fuel, oil)
DESCRIBE THE BMP'S THAT WILL BE PROVIDED TO MINIMIZE STORMWATER POLLUTION FROM THE POTENTIAL POLLUTION SOURCE.
Pre-inspect equipment, remove from operation if leak develops.
POTENTIAL POLLUTANT SOURCE 2
WHAT IS THE LOCATION OF THE POTENTIAL POLLUTANT SOURCE? (e.g. ROUTE, MILEPOST, OR STATION)
Project wide
DESCRIBE THE POTENTIAL POLLUTANT SOURCE AND ITS POLLUTANTS OF CONCERN.
Debris from general operations
DESCRIBE THE BMP'S THAT WILL BE PROVIDED TO MINIMIZE STORMWATER POLLUTION FROM THE POTENTIAL POLLUTION SOURCE.
Maintain housekeeping, wattles/silt fence to protect nearby waterway, di covers if necessary

POTENTIAL POLLUTANT SOURCE 3
WHAT IS THE LOCATION OF THE POTENTIAL POLLUTANT SOURCE? (e.g. ROUTE, MILEPOST, OR STATION)
Project wide
DESCRIBE THE POTENTIAL POLLUTANT SOURCE AND ITS POLLUTANTS OF CONCERN.
Dust
DESCRIBE THE BMP'S THAT WILL BE PROVIDED TO MINIMIZE STORMWATER POLLUTION FROM THE POTENTIAL POLLUTION SOURCE.
Water truck, cease activities in high winds
POTENTIAL POLLUTANT SOURCE 4
WHAT IS THE LOCATION OF THE POTENTIAL POLLUTANT SOURCE? (e.g. ROUTE, MILEPOST, OR STATION)
Bridge Deck
DESCRIBE THE POTENTIAL POLLUTANT SOURCE AND ITS POLLUTANTS OF CONCERN.
Polymer materials
DESCRIBE THE BMP'S THAT WILL BE PROVIDED TO MINIMIZE STORMWATER POLLUTION FROM THE POTENTIAL POLLUTION SOURCE.
training/precise application, wattles if necessary, specialized application equipment

ATTACH ADDITIONAL PAGES WHEN NECESSARY TO PROVIDE THE REQUIRED INFORMATION.

SPILL PREVENTION AND RESPONSE

MATERIALS STORAGE, SPILL PREVENTION AND RESPONSE

PROVIDE A DESCRIPTION OF THE CONSTRUCTION MATERIALS AND CHEMICALS THAT ARE EXPECTED TO BE STORED ONSITE, WITH UPDATES AS APPROPRIATE. DESCRIBE THE BMPs THAT WILL BE PROVIDED TO ENSURE PROPER STORAGE OF THESE CONSTRUCTION MATERIALS AND WILL MINIMIZE THEIR EXPOSURE TO STORMWATER. DESCRIBE THE PROCEDURES TO PREVENT AND RESPOND TO SPILLS, LEAKS, AND OTHER RELEASES. OTHER EXISTING SPILL PREVENTION PLANS, SUCH AS THE SPILL PREVENTION CONTROL AND COUNTERMEASURE (SPCC) PLANS DEVELOPED FOR THE CONSTRUCTION ACTIVITY UNDER PART 311 OF THE CLEAN WATER ACT (CWA), OR SPILL CONTROL PROGRAMS OTHERWISE REQUIRED BY NDEP PERMITS FOR THE CONSTRUCTION ACTIVITY, MAY BE REFERENCED IN THE SWPPP PROVIDED THAT COPIES OF THESE DOCUMENTS ARE KEPT ONSITE.

CONTAINER LABELING

DESCRIBE PROCEDURES FOR PLAINLY LABELING CONTAINERS (E.G. USED OIL, PESTICIDES, ETC.) THAT COULD BE SUSCEPTIBLE TO SPILLAGE OR LEAKAGE TO ENCOURAGE PROPER HANDLING AND FACILITATE RAPID RESPONSE IN THE EVENT SPILLS OR LEAKS OCCUR.

MSDS sheets available for any hazardous materials on-site. All such materials will be separated, labeled, and stored properly.

PREVENTATIVE MEASURES

DESCRIBE PREVENTATIVE MEASURES SUCH AS BARRIERS BETWEEN MATERIAL STORAGE AND TRAFFIC AREAS, SECONDARY CONTAINMENT PROVISIONS, AND GENERAL PROCEDURES FOR MATERIAL STORAGE AND HANDLING.

Any chemicals will be stored in a locked Q&D Construction conex (contained) or at a permitted off site facility that is not solely dedicated to this job. Any chemicals will be properly stored with no danger of being exposed to storm water or weather.

SPILL/LEAK STOPPAGE, CONTAINMENT AND CLEANING

DESCRIBE PROCEDURES FOR EXPEDITIOUSLY STOPPING, CONTAINING, AND CLEANING UP SPILLS, LEAKS, AND OTHER RELEASES. IDENTIFY THE NAME AND POSITION OF THE EMPLOYEE(S) RESPONSIBLE FOR DETECTING AND RESPONDING TO SPILL OR LEAKS.

It is everyone's responsibility on the job site to detect spills/leaks. As soon as a spill/leak is detected, foreman, PM, Superintendent, or other leadership personnel will be notified immediately so they can then assess the situation and contact the appropriate emergency response agencies.

SPILL/LEAK NOTIFICATION

DESCRIBE PROCEDURES FOR NOTIFICATION OF APPROPRIATE FACILITY PERSONNEL, EMERGENCY RESPONSE AGENCIES, AND REGULATORY AGENCIES WHERE A LEAK, SPILL, OR OTHER RELEASE CONTAINING A HAZARDOUS SUBSTANCE OR OIL IN AN AMOUNT EQUAL TO OR IN EXCESS OF A REPORTABLE QUANTITY ESTABLISHED UNDER 40 CODE OF FEDERAL REGULATIONS (CFR) PART 110, 40 CFR PART 117, OR 40 CFR PART 302, OCCURS DURING A 24-HOUR PERIOD. CONTACT INFORMATION OF THE APPROPRIATE PERSONNEL SHALL BE POSTED IN LOCATIONS THAT ARE READILY ACCESSIBLE AND AVAILABLE.

See above.

FACILITY PERSONNEL

Project general superintendent should be notified first Scott Leone. Will then proceed to notify James McCain (Safety Director), Gracie Damele (Environmental Engineer/WPCM), and Braden Riley (Project Manager) as well as any necessary emergency response agencies.

EMERGENCY RESPONSE AGENCIES

911
Clean Harbors 775 624 8060
Graymar (866) GRAYMAR
After Hours: (866) 472-9627

REGULATORY AGENCIES

NDEP Spill hotline 1-888-331-6337

WASTE MANAGEMENT PROCEDURES

CONSTRUCTION WASTE STORAGE AND DISPOSAL

DESCRIBE THE CONSTRUCTION WASTES THAT ARE EXPECTED TO BE GENERATED ONSITE. CONSTRUCTION WASTE INCLUDE CONCRETE WASHOUT, EXCESS BUILDING MATERIALS, CHEMICALS, AND SEDIMENT REMOVED FROM THE SITE, LITTER AND DEBRIS. DESCRIBE THE BMPs THAT WILL BE USED TO TEMPORARILY STORE THESE WASTES, AND HOW THEY WILL BE COLLECTED AND DISPOSED.

Dumpsters will be on site to dispose of any and all waste that is not hazardous or toxic. Hazardous or toxic waste will be disposed of in seal-able drum containers and then dropped off at an appropriate hazard waste facility.

HAZARDOUS MATERIAL AND SANITARY WASTE STORAGE AND DISPOSAL

PROVIDE A DESCRIPTION OF HAZARDOUS AND SANITARY OR SEPTIC WASTES THAT ARE EXPECTED TO BE GENERATED ONSITE. DESCRIBE HOW THESE WASTES WILL BE TEMPORARILY STORED, COLLECTED AND DISPOSED.

No waste should be generated onsite. Portable bathrooms will be keyed into the ground. Any hazardous waste will be kept in primary & secondary containment.

VEHICLE TRACK-OUT CONTROLS

PROVIDE A DESCRIPTION OF THE CONTROL MEASURES THAT WILL BE IMPLEMENTED TO CONTROL TRACK-OUT AND THE MEASURES THAT WILL BE USED TO REMOVE ANY SEDIMENTS THAT HAVE BEEN DEPOSITED ON PAVED SURFACES FROM CONSTRUCTION EQUIPMENT EXITING THE PROJECT AREA.

To minimize track-out we may use a stabilized construction entrance to reduce sediments on streets and sidewalks.

POST CONSTRUCTION STORMWATER MANAGEMENT

STORMWATER MANAGEMENT CONTROLS

PROVIDE A DESCRIPTION OF THE MEASURES INSTALLED DURING CONSTRUCTION THAT WILL BE USED TO CONTROL POLLUTANTS IN STORMWATER DISCHARGES BETWEEN THE TIME CONSTRUCTION ACTIVITIES HAVE CEASED AND FINAL SITE STABILIZATION HAS BEEN ACHIEVED. THESE STORMWATER MANAGEMENT CONTROLS INCLUDE BUT ARE NOT LIMITED TO SEDIMENT RETENTION BASINS, INFILTRATION TRENCHES, VEGETATED SWALES AND RIP RAP.

LOCATION/AREA	CONTROL MEASURE
Used for secondary containment of polymer materials	Visqueen
Used to keep dust down	Water Trucks
Used to keep roads clean of track-out	Sweeper Truck

INSPECTION/MAINTENANCE PROCEDURES

THE CONTRACTOR OR HIS QUALIFIED AGENT IS REQUIRED TO INSPECT ALL DISTURBED AREAS, AREAS USED FOR STORAGE OF MATERIALS AND EQUIPMENT THAT ARE EXPOSED TO PRECIPITATION, VEHICLE ENTRANCE AND EXIT LOCATIONS AND ALL EROSION AND SEDIMENT CONTROL BMPs. INSPECTIONS SHALL AT A MINIMUM OCCUR WEEKLY, PRIOR TO FORECASTED RAIN EVENTS, AND WITHIN 24 HOURS AFTER A RAIN EVENT OF 0.25 INCHES OR GREATER DURING A 24 HOUR PERIOD. **NDOT SPECIFICATIONS REQUIRE PLACEMENT OF A RAIN GAUGE ON ALL PROJECTS TO MEASURE THE ACTUAL RAINFALL.**

1. INSPECTION PROCEDURES

DESCRIBE THE PRACTICES, PROCEDURES, AND PROTOCOLS OPERATORS WILL FOLLOW FOR CONDUCTING SITE INSPECTIONS.

Foreman (TBD) will perform job site walks at minimum on a weekly basis to ensure all BMPs on the job site have been properly installed and are in good working order and condition. Any defective BMPs will be repaired or replaced, and any additional areas requiring BMPs will be identified at this time. BMP maintenance will also be performed prior to, during, and after any potential storm events.

IDENTIFY THE PERSONNEL RESPONSIBLE FOR CONDUCTING THE INSPECTIONS.

See above.

PROVIDE THE INSPECTION SCHEDULE THAT WILL BE FOLLOWED BASED ON WHETHER THE SITE IS SUBJECT TO ROUTINE INSPECTION FREQUENCY, OR WHETHER THE SITE QUALIFIES FOR A REDUCED INSPECTION FREQUENCY PER THE APPLICABLE CONSTRUCTION GENERAL PERMIT. IF THE SITE (OR PORTIONS OF THE SITE) QUALIFIES FOR A REDUCED INSPECTION SCHEDULE INCLUDE THE BEGINNING AND ENDING DATES OF THE REDUCED INSPECTION PERIOD.

Site inspection will be performed weekly at minimum. BMPs will also be checked prior to, during, and after any storm events if it is safe to do so.

2. INSPECTION DOCUMENTATION

ATTACH ALL INSPECTION DOCUMENTATION TO THE SWPPP. ATTACH ALL DOCUMENTED FINDINGS FOR EACH SITE INSPECTION TO THE END OF THE SWPPP. INSPECTION DOCUMENTATION REQUIREMENTS ARE OUTLINED IN THE APPLICABLE PERMIT. NDOT SPECIFICATIONS REQUIRE THE USE OF THE DEPARTMENT FURNISHED INSPECTION FORM. INCLUDE INSPECTION FORMS, RECORDS OF CORRECTIVE ACTIONS, ETC.

3. MAINTENANCE PROCEDURES

DESCRIBE MAINTENANCE PROCEDURES THAT OPERATORS WILL FOLLOW FOR MAINTAINING THEIR STORMWATER CONTROL MEASURES.

Construction activities (heavy equipment) will cease during high wind events. Water trucks will be utilized during grading and excavation or trenching activities that disturb native soil. Track out aprons may also be utilized to prevent soil from entering adjacent roadways.

4. CORRECTIVE ACTION PROCEDURES

DESCRIBE THE PRACTICES, PROCEDURES, PROTOCOLS OPERATORS WILL FOLLOW FOR TAKING ANY NECESSARY CORRECTIVE ACTIONS. "Corrective Action" – as defined in the permits means: any action taken to (1) repair, modify, or replace any stormwater control used at the site; (2) clean up and dispose of spills, releases, or other deposits found on the site; and (3) remedy a permit violation.

Work will be stopped, the situation will be assessed and proper action will be taken to remedy the situation.

ADDITIONAL INFORMATION

PROVIDE ANY ADDITIONAL PERTINENT INFORMATION.

1. CONTROL MEASURE ADDITION/REPAIR/MODIFICATION

FOLLOWING AN INSPECTION IN ACCORDANCE WITH THE APPLICABLE PERMIT, IF IT IS DETERMINED THAT THE INSTALLATION OF ADDITIONAL CONTROL MEASURES, OR SIGNIFICANT REPAIR OR MODIFICATION OF AN EXISTING CONTROL MEASURE IS REQUIRED, AND IMPLEMENTATION BEFORE THE NEXT STORM EVENT IS IMPRACTICAL, DOCUMENT THE REASON(S) FOR THE DELAY.

Will be documented in the inspection report if need be.

IDENTIFY AND DESCRIBE THE MODIFICATIONS MADE TO THE CONTROL MEASURES.

Will be documented in the inspection report if need be.

2. DEPARTURES FROM DESIGN SPECIFICATIONS

EXPLAIN ANY DEPARTURES FROM DESIGN SPECIFICATIONS FOR THE INSTALLATION OF STORMWATER CONTROL MEASURES.

See attached site map for any alterations.

3. CULVERT STABILIZATION

IF CULVERTS ARE PRESENT ON THE SITE, DESCRIBE THE MEASURES IMPLEMENTED TO SUFFICIENTLY MINIMIZE THE THREAT OF EROSION AT CULVERT LOCATIONS TO PREVENT THE FORMATION OF RILLS AND GULLIES DURING CONSTRUCTION.

N/A

4. SPECIAL CONSTRUCTION DISTURBANCES

IF THE PROJECT INVOLVES CONSTRUCTION APPROVED UNDER A CWA SECTION 404 PERMIT, WORKING IN WATERWAY PERMIT, OR CONSTRUCTION OF A WATER-DEPENDENT STRUCTURE OR WATER ACCESS AREA (E.G. PIER, BOAT RAMP, TRAIL), DOCUMENT THE CONSTRUCTION BELOW AND MAKE SPECIFIC REFERENCE TO THIS ON THE SITE MAP.

If Q&D is in special areas it will be documented & an applicable permit will be applied for.

5. LINEAR CONSTRUCTION PROJECTS

FOR PERIMETER CONTROLS ON LINEAR CONSTRUCTION PROJECTS WHERE IT IS INFEASIBLE TO COMPLY WITH THE REQUIREMENTS OF THE CGP, DOCUMENT THE CIRCUMSTANCES AND RATIONALE FOR WHY IT IS INFEASIBLE TO DO SO, AND DESCRIBE ANY BUFFER WIDTH RETAINED AND/OR SUPPLEMENTAL EROSION CONTROLS INSTALLED.

N/A

FOR LINEAR CONSTRUCTION PROJECTS WITH RIGHT-OF-WAY THAT RESTRICTS OR THAT PREVENT THE USE OF PERIMETER CONTROLS REQUIRED BY THE PERMIT, IDENTIFY THESE AREAS AND EXPLAIN WHY IT IS IMPRACTICAL TO MAXIMIZE THE USE OF PERIMETER CONTROLS.

See above.

a. TRACK-OUT (LINEAR CONSTRUCTION PROJECTS)

IF SITE CONDITIONS MAKE IT INFEASIBLE TO INSTALL STRUCTURAL CONTROLS TO PREVENT TRACK-OUT (E.G. LINEAR PAVING PROJECT), EXPLAIN WHY SUCH CONTROLS CANNOT BE INSTALLED AND DESCRIBE THE ALTERNATIVE MEASURES THAT WILL BE USED TO PREVENT, MONITOR AND REMEDIATE TRACK-OUT SEDIMENT FROM ROADWAYS.

Track out aprons will be installed where necessary. Sweeper will be used to clean up track out.

6. SEDIMENT OR STOCKPILES

IF IT IS INFEASIBLE TO PLACE SEDIMENT OR STOCKPILES AWAY FROM STORMWATER CONVEYANCES EXPLAIN WHY IT IS INFEASIBLE TO DO SO AND NOTE THE APPROPRIATE SEDIMENT CONTROL MEASURES SELECTED AND DESCRIBE ADDITIONAL OR ENHANCED CONTROL MEASURES TO MINIMIZE DISCHARGES FROM STOCKPILES.

Any stockpiled material requiring protection will utilize proper BMP techniques to prevent unwarranted run off (wattles).

7. NON-VEGETATIVE FINAL STABILIZATION METHODS

DESCRIBE ALL NON-VEGETATIVE STABILIZATION METHODS EMPLOYED ON THE SITE FOR FINAL STABILIZATION.

Paving, concrete

8. DISCHARGES TO IMPAIRED WATERBODIES WITHOUT ESTABLISHED TOTAL MAXIMUM DAILY LOADS

IF THE SITE DISCHARGES TO A WATER QUALITY-IMPAIRED WATER IN THE CURRENT 303(D) IMPAIRED WATER BODY LISTING FOR WHICH THERE IS NO TOTAL MAXIMUM DAILY LOAD ESTABLISHED, DESCRIBE THE CONDITION FOR WHICH THE WATER HAS BEEN LISTED AND INCLUDE A DEMONSTRATION THAT THE BMPS THAT ARE SELECTED FOR IMPLEMENTATION WILL BE SUFFICIENT TO ENSURE THAT DISCHARGES WILL NOT CAUSE OR CONTRIBUTE TO AN EXCEEDANCE OF AN APPLICABLE WATER QUALITY STANDARD.

N/A

9. DISCHARGES TO IMPAIRED WATERBODIES WITH ESTABLISHED TOTAL MAXIMUM DAILY LOADS

IF THE SITE DISCHARGES TO A WATERBODY WITH AN ESTABLISHED TOTAL MAXIMUM DAILY LOAD (TMDL) COMPLY WITH ALL APPLICABLE TMDL REQUIREMENTS. IF A TMDL HAS NOT BEEN ESTABLISHED, DESCRIBE THE CONDITION FOR WHICH THE WATER HAS BEEN LISTED AND INCLUDE A DEMONSTRATION THAT THE BMPS THAT ARE SELECTED FOR IMPLEMENTATION WILL BE SUFFICIENT TO ENSURE THAT DISCHARGES WILL NOT CAUSE OR CONTRIBUTE TO AN EXCEEDANCE OF AN APPLICABLE STATE WATER QUALITY STANDARD.

N/A

10. SEDIMENT BASIN DISCHARGES

IF UTILIZING OUTLET STRUCTURES TO WITHDRAW WATER FROM THE SURFACE OF A SEDIMENT BASIN IN ORDER TO MINIMIZE THE DISCHARGE OF POLLUTANTS IS DETERMINED TO BE INFEASIBLE, EXPLAIN WHY IT INFEASIBLE AND ATTACH ANY PERTINENT DOCUMENTATION TO THE END OF THE SWPPP.

N/A

11. ADDITIONAL DISCHARGE REQUIREMENTS

WHERE NDEP OR THE EPA DETERMINES IT IS NECESSARY TO IMPOSE ADDITIONAL REQUIREMENTS TO DISCHARGE, ATTACH A COPY OF ANY CORRESPONDENCE DESCRIBING SUCH REQUIREMENTS TO THE END OF THE SWPPP, AND DESCRIBE THE STORMWATER CONTROL MEASURES THAT WILL BE USED TO MEET SUCH REQUIREMENTS.

N/A

DOCUMENTATION REQUIREMENTS

PROVIDE THE FOLLOWING INFORMATION.

1. NOTICE OF INTENT (NOI)

ATTACH A COPY OF THE SIGNED ELECTRONIC NOI CERTIFICATION PAGE SUBMITTED TO THE NDEP AND/OR (EPA FOR TRIBAL LANDS) TO THE END OF THE SWPPP.

2. APPROVAL LETTER

ATTACH A COPY OF THE APPROVAL LETTER RECEIVED FROM NDEP AND/OR EPA TO THE END OF THE SWPPP.

3. PERMIT

ATTACH A COPY OF THE PERMIT TO THE END OF THE SWPPP.

4. SIGNIFICANT SPILLS/LEAKS/RELEASES

DESCRIBE ANY INCIDENCES OF SIGNIFICANT SPILLS LEAKS, OR OTHER RELEASES THAT RESULTED IN DISCHARGES OF POLLUTANTS IN STORMWATER TO A REGULATED MS4 OR WATERS OF THE STATE OF NEVADA THAT MEET THE DEFINITION OF WATERS OF THE U.S. INCLUDE THE DATE OF THE OCCURRENCE, THE CIRCUMSTANCES LEADING TO THE RELEASE, ACTIONS TAKEN IN RESPONSE TO THE RELEASE, AND MEASURES IMPLEMENTED TO PREVENT RECURRENCE OF SUCH RELEASE(S).

N/A

5. STRUCTURAL CONTROL MEASURE REPAIRS

ATTACH TO THE END OF THE SWPPP, DOCUMENTATION OF REPAIRS MADE TO STRUCTURAL CONTROL MEASURES. THIS DOCUMENTATION SHALL INCLUDE THE DATE(S) OF DISCOVERY OF AREAS IN NEED OF REPAIR/REPLACEMENT, DATE(S) THAT THE STRUCTURAL CONTROL MEASURE(S) RETURNED TO FULL FUNCTION, AND JUSTIFICATION FOR PROLONGED REPAIR SCHEDULES.

6. INSPECTION REPORTS

ATTACH A COPY OF ALL SELF-PERFORMED INSPECTION REPORTS TO THE END OF THE SWPPP.

7. CORRECTIVE ACTION

DESCRIBE ANY CORRECTIVE ACTIONS TAKEN AT THE SITE. INCLUDE EVENTS AND DATES WHEN PROBLEMS WERE DISCOVERED AND WHAT MODIFICATIONS OCCURRED.

N/A

8. BUFFER DOCUMENTATION
IF THE SITE'S DISTURBANCE AREA IS LOCATED WITHIN 50-FEET OF SURFACE WATER, ATTACH BUFFER DOCUMENTATION TO THE END OF THE SWPPP.
9. EMPLOYEE TRAINING RECORDS/CERTIFICATIONS
ATTACH RECORDS OF THE EMPLOYEE TRAINING/CERTIFICATION TO THE END OF THE SWPPP. RECORDS SHALL INCLUDE THE DATE THE TRAINING WAS RECEIVED AND APPLICABLE EXPIRATION DATES.
10. PLANS REQUIRED BY OTHER AGENCIES
THE SWPPP MAY INCORPORATE BY REFERENCE THE APPROPRIATE ELEMENTS OF PLANS REQUIRED BY OTHER AGENCIES. ATTACH A COPY OF THE REQUIREMENTS INCORPORATED BY REFERENCE TO THE END OF THE SWPPP.
11. DEMINIMIS DISCHARGES
FOR DEMINIMIS DISCHARGES COVERED UNDER THE NDEP CGP, DESCRIBE THE DISCHARGE, PROVIDE THE BEGINNING AND END DATES OF THE DISCHARGE, AND ATTACH TO THE END OF THE SWPPP A COPY OF ALL RELATIVE DOCUMENTATION TO INCLUDE BUT NOT BE LIMITED TO COPIES OF ALL DISCHARGE MONITORING REPORTS, CHAIN OF CUSTODY FORMS AND THE LABORATORY ANALYSIS

DOCUMENTATION OF COMPLIANCE WITH EPA CGP REQUIRED PERMITTED SITES (Tribal Lands)

PROVIDE THE FOLLOWING DOCUMENTATION AS AN ATTACHEMENT
1. ENDANGERED SPECIES PROTECTION
Instructions (see EPA CGP Parts 1.1.e, 7.2.14.1, Appendix D, and the "Endangered Species Protection" section of the Appendix J – NOI form)
2. HISTORIC PRESERVATION
Instructions (see EPA CGP Part 1.1.f, 7.2.14.2, Appendix E, and the "Historic Preservation" section of the Appendix J – NOI form)
3. SAFE DRINKING WATER ACT UNDERGROUND INJECTION CONTROL REQUIREMENTS
Instructions (see CGP Part 7.2.14.3): — If you will use any of the identified controls in this section, include documentation of contact between you and the EPA Regional Office responsible for implementing the requirements for underground injection wells in the Safe Drinking Water Act and EPA's implementing regulations at 40 CFR Parts 144-147.

CERTIFICATIONS OF COMPLIANCE

THIS SWPPP MUST BE CERTIFIED THAT IT IS CONSISTENT WITH ALL APPLICABLE FEDERAL, STATE AND LOCAL REGULATIONS, OR OTHER APPROVED SITE PLANS OR PERMITS. IT IS TO BE PREPARED IN ACCORDANCE WITH THE NEVADA DEPARTMENT OF TRANSPORTATION BEST MANAGEMENT PRACTICES (BMPS) MANUAL. THIS SWPPP MUST BE UPDATED AS NECESSARY TO REMAIN CONSISTENT WITH CHANGES IN OTHER SITE PLANS THAT EFFECT SOIL DISTURBING ACTIVITIES, SITE DRAINAGE PATTERNS OR ANY OTHER ACTIVITY THAT MAY IMPACT STORMWATER RUNOFF QUALITY. IT MUST ALSO BE RE-CERTIFIED ANNUALLY BY JULY 1 UNTIL THE CONSTRUCTION PROJECT IS COMPLETE AND A NOTICE OF TERMINATION HAS BEEN SUBMITTED TO NDEP.

1. OWNER/OPERATOR CERTIFICATION STATEMENT

I CERTIFY UNDER PENALTY OF LAW THAT THIS DOCUMENT AND ALL ATTACHMENTS WERE PREPARED UNDER MY DIRECTION OR SUPERVISION IN ACCORDANCE WITH A SYSTEM DESIGNED TO ASSURE THAT QUALIFIED PERSONNEL PROPERLY GATHER AND EVALUATE THE INFORMATION SUBMITTED. BASED ON MY INQUIRY OF THE PERSON OR PERSONS WHO MANAGE THE SYSTEM, OR THOSE PERSONS DIRECTLY RESPONSIBLE FOR GATHERING THE INFORMATION, THE INFORMATION SUBMITTED IS, TO THE BEST OF MY KNOWLEDGE AND BELIEF, TRUE, ACCURATE, AND COMPLETE. I AM AWARE THAT THERE ARE SIGNIFICANT PENALTIES FOR SUBMITTING FALSE INFORMATION, INCLUDING THE POSSIBILITY OF FINE AND IMPRISONMENT FOR KNOWING VIOLATIONS.

INITIAL CERTIFICATION:

Gracie Damele

Environmental Compliance Engineer

PRINT NAME

TITLE

SIGNATURE

DATE

ANNUAL RE-CERTIFICATION:

PRINT NAME

TITLE

SIGNATURE

DATE

ALL CONTRACTORS AND SUBCONTRACTORS RESPONSIBLE FOR IMPLEMENTING POLLUTION CONTROL MEASURES MUST BE IDENTIFIED IN THIS SWPPP WITH THE MEASURES FOR WHICH THEY ARE RESPONSIBLE. THEY MUST ALSO SIGN THE FOLLOWING CERTIFICATION STATEMENT THAT INDICATES THEY UNDERSTAND THE REQUIREMENTS OF THE STATE'S GENERAL PERMIT FOR CONSTRUCTION ACTIVITIES (ATTACH COPY OF PERMIT).

2. CONTRACTOR'S CERTIFICATION STATEMENT

I CERTIFY UNDER PENALTY OF LAW THAT I UNDERSTAND THE TERMS AND CONDITIONS OF THE STATE'S GENERAL PERMIT (NVR100000) THAT AUTHORIZES STORMWATER DISCHARGES ASSOCIATED WITH INDUSTRIAL ACTIVITY FROM THE CONSTRUCTION SITE IDENTIFIED AS PART OF THIS CERTIFICATION.

NDOT	1263 S Stewart St
------	-------------------

COMPANY 1

ADDRESS

Carson City	Nevada	7754314672
-------------	--------	------------

CITY

STATE

PHONE NO.

David Knight

Resident Engineer

PRINT NAME

TITLE

SIGNATURE

DATE

RESPONSIBILITIES

Q&D Construction

1050 S 21st St

COMPANY 2

ADDRESS

Sparks	Nevada	7753026540
--------	--------	------------

CITY

STATE

PHONE NO.

Scott Leone

Superintendent

PRINT NAME


TITLE

SIGNATURE

DATE

RESPONSIBILITIES

Disturbance Area



G-884

G-885

I-80

Humboldt River

UPRR

UPRR

G-886

Humboldt River





NEVADA DIVISION OF
**ENVIRONMENTAL
PROTECTION**

STATE OF NEVADA
Department of Conservation & Natural Resources

Joe Lombardo, *Governor*
James A. Settelmeyer, *Director*
Jennifer L. Carr, *Administrator*

Date: 2/10/2025

Mr. David Knight
NDOT
1263 S Stewart Street
Carson City NV 89712

Dear Mr. David Knight
Re: Stormwater Construction Permit
Project ID Number: CSW--55080
Project Name: NDOT 4529 I-80 Dunphy

Your submittal to be included under this General Permit has been approved effective 2/10/2025. For Stormwater Permits, please note that by submitting an NOI the permittee has certified that the project's Storm Water Pollution Prevention Plan (SWPPP) has been completed, that the SWPPP will be updated as necessary, and that it will be maintained at the permitted site.

At the time of any on-site inspections, our inspectors will ask to review your copy of the SWPPP in an effort to ensure proper compliance with the program.

Also note that Nevada Administrative Code (NAC) 445A.268 Section (5)(b) reads, in part, that a Permittee (discharger) who is covered under a general permit shall pay to the Director a nonrefundable fee of \$200.00 not later than July 1 of each year that the discharger is covered under that permit.

To Terminate coverage of this Nevada General Permit, the Permittee must submit a Notice of Termination ("NOT") form when their facility no longer has any discharges associated with this Nevada General Permit or EPA regulations at 40 CFR 122.26, or when they are no longer the operator of the site.

Questions regarding Stormwater permits, please contact (775) 687-9442.

Questions regarding other general permits, please contact (775) 687-9492.

Sincerely,

Kristie Black, Supervisor

Bureau of Water Pollution Control
Nevada Division of Environmental Protection

CC: Mr. Scott Leone 1050 S 21st St Sparks NV 89431

RECEIVED
FEB 13 2025

O & D Construction

NVR100000
STATE OF NEVADA
DIVISION OF ENVIRONMENTAL PROTECTION
GENERAL PERMIT

FOR

**STORMWATER DISCHARGES ASSOCIATED WITH LARGE CONSTRUCTION ACTIVITY, SMALL
CONSTRUCTION ACTIVITY AND INDUSTRIAL ACTIVITY FROM TEMPORARY CONCRETE, ASPHALT
AND
MATERIAL PLANTS OR OPERATIONS DEDICATED TO THE PERMITTED CONSTRUCTION
PROJECT**

AUTHORIZATION TO DISCHARGE

In compliance with the provisions of the federal Water Pollution Control Act as amended (33 U.S.C. 1251 et seq: the "Act") and Chapter 445A of the Nevada Revised Statutes (NRS), eligible dischargers have submitted: 1) a Notice of Intent and filing fee in accordance with Nevada Administrative Code (NAC) 445A.268.

In accordance with the terms and conditions set forth hereof;

Site Number: CSW-55080

NOI Approval Date: 2/10/2025


NOI Re-Approval Date: N/A

Facility Information	
Site Name	NDOT 4529 I-80 Dunphy
Site Address	I-80 MP EU 4.120 to 4.950, Dunphy, NV 89820-_____
Owner Name	NDOT
Operator Name	Q&D Construction LLC

This permit shall become effective on: **January 5, 2015.**

This permit and the authorization to discharge shall expire at midnight **January 4, 2020.**

Signed this **5th** day of **January 2015.**



Michele R. Reid, Staff II Associate Engineer
Bureau of Water Pollution Control

Review/Print The Entered Information Before Clicking Submit Button Below

(Note: The entered information will be locked after Submit is clicked)

New Permit: CSW-55080

Section 1

Facility / Site Information

Estimated Area to be Disturbed (in acres): **1.50**
Site Name: **NDOT 4529 I-80 Dunphy**
Address Line 1: **I-80 MP EU 4.120 to 4.950**
Address Line 2:
City / State / Zipcode: **Dunphy, NV 89820-_____**
Contact Name (Phone #): **Mr.Scott Leone (7753026540)**
Email: **sleone@qdconstruction.com**
Name of Receiving Water and /or Description of Discharge Location: **Humboldt River**
Frequency of Discharge: **Unlikely**
Estimated Flow in Gallons: **0**
Estimated Begin - End Date: **03/13/2025 - 06/30/2025**

SWPPP Information

Address Line 1: **I-80 MP EU 4.120 to 4.950**
Address Line 2:
City State / Zipcode: **Dunphy, NV 89820-_____**
Contact Name (Phone #): **Mr.Scott Leone (7753026540)**

Location / GIS Information

Latitude / Longitude: **40.698386° / -116.516592°**
Assessor's Parcel Number (APN): **near 422009**
Standard Industrial Classification (SIC) Code: **CNST - Construction General Permit**
County(ies): **Eureka**

Section 2, 3 And 4

Owner Name and Address

Is the Owner the Permittee? - **NO**
Owner Name: **NDOT**
Address Line 1: **1263 S Stewart Street**
Address Line 2:
City / State / Zipcode: **Carson City, NV 89712**
Contact Name: **Mr.David Knight**
Contact Phone #: **7754314672**
Taxpayer ID (TIN): **0**
Legal Status: **State**

Operator Name and Address

Is the Operator the Permittee? - **YES**
Operator Name: **Q&D Construction LLC**
Address Line 1: **1050 S 21st St**
Address Line 2:
City / State / Zipcode: **Sparks, NV 89431**
Contact Name: **Mr.Scott Leone**
Contact Phone #: **7753026540**
Taxpayer ID (TIN): **0**
Legal Status: **Federal**

Billing/Invoicing

Send Annual Billing/Invoicing Information to: **Operator**


Attachments

Attached File Name: **N/A**

Section 5

Additional / Consultant Contact Information (Optional)

Company/Name	Address 1	Address 2	City	State	Zip	Title	First Name	Last Name	Contact Phone
Q&D Construction LLC	1050 S 21st St		Sparks	NV	89431	Ms.	Gracie	Damele	7753026407

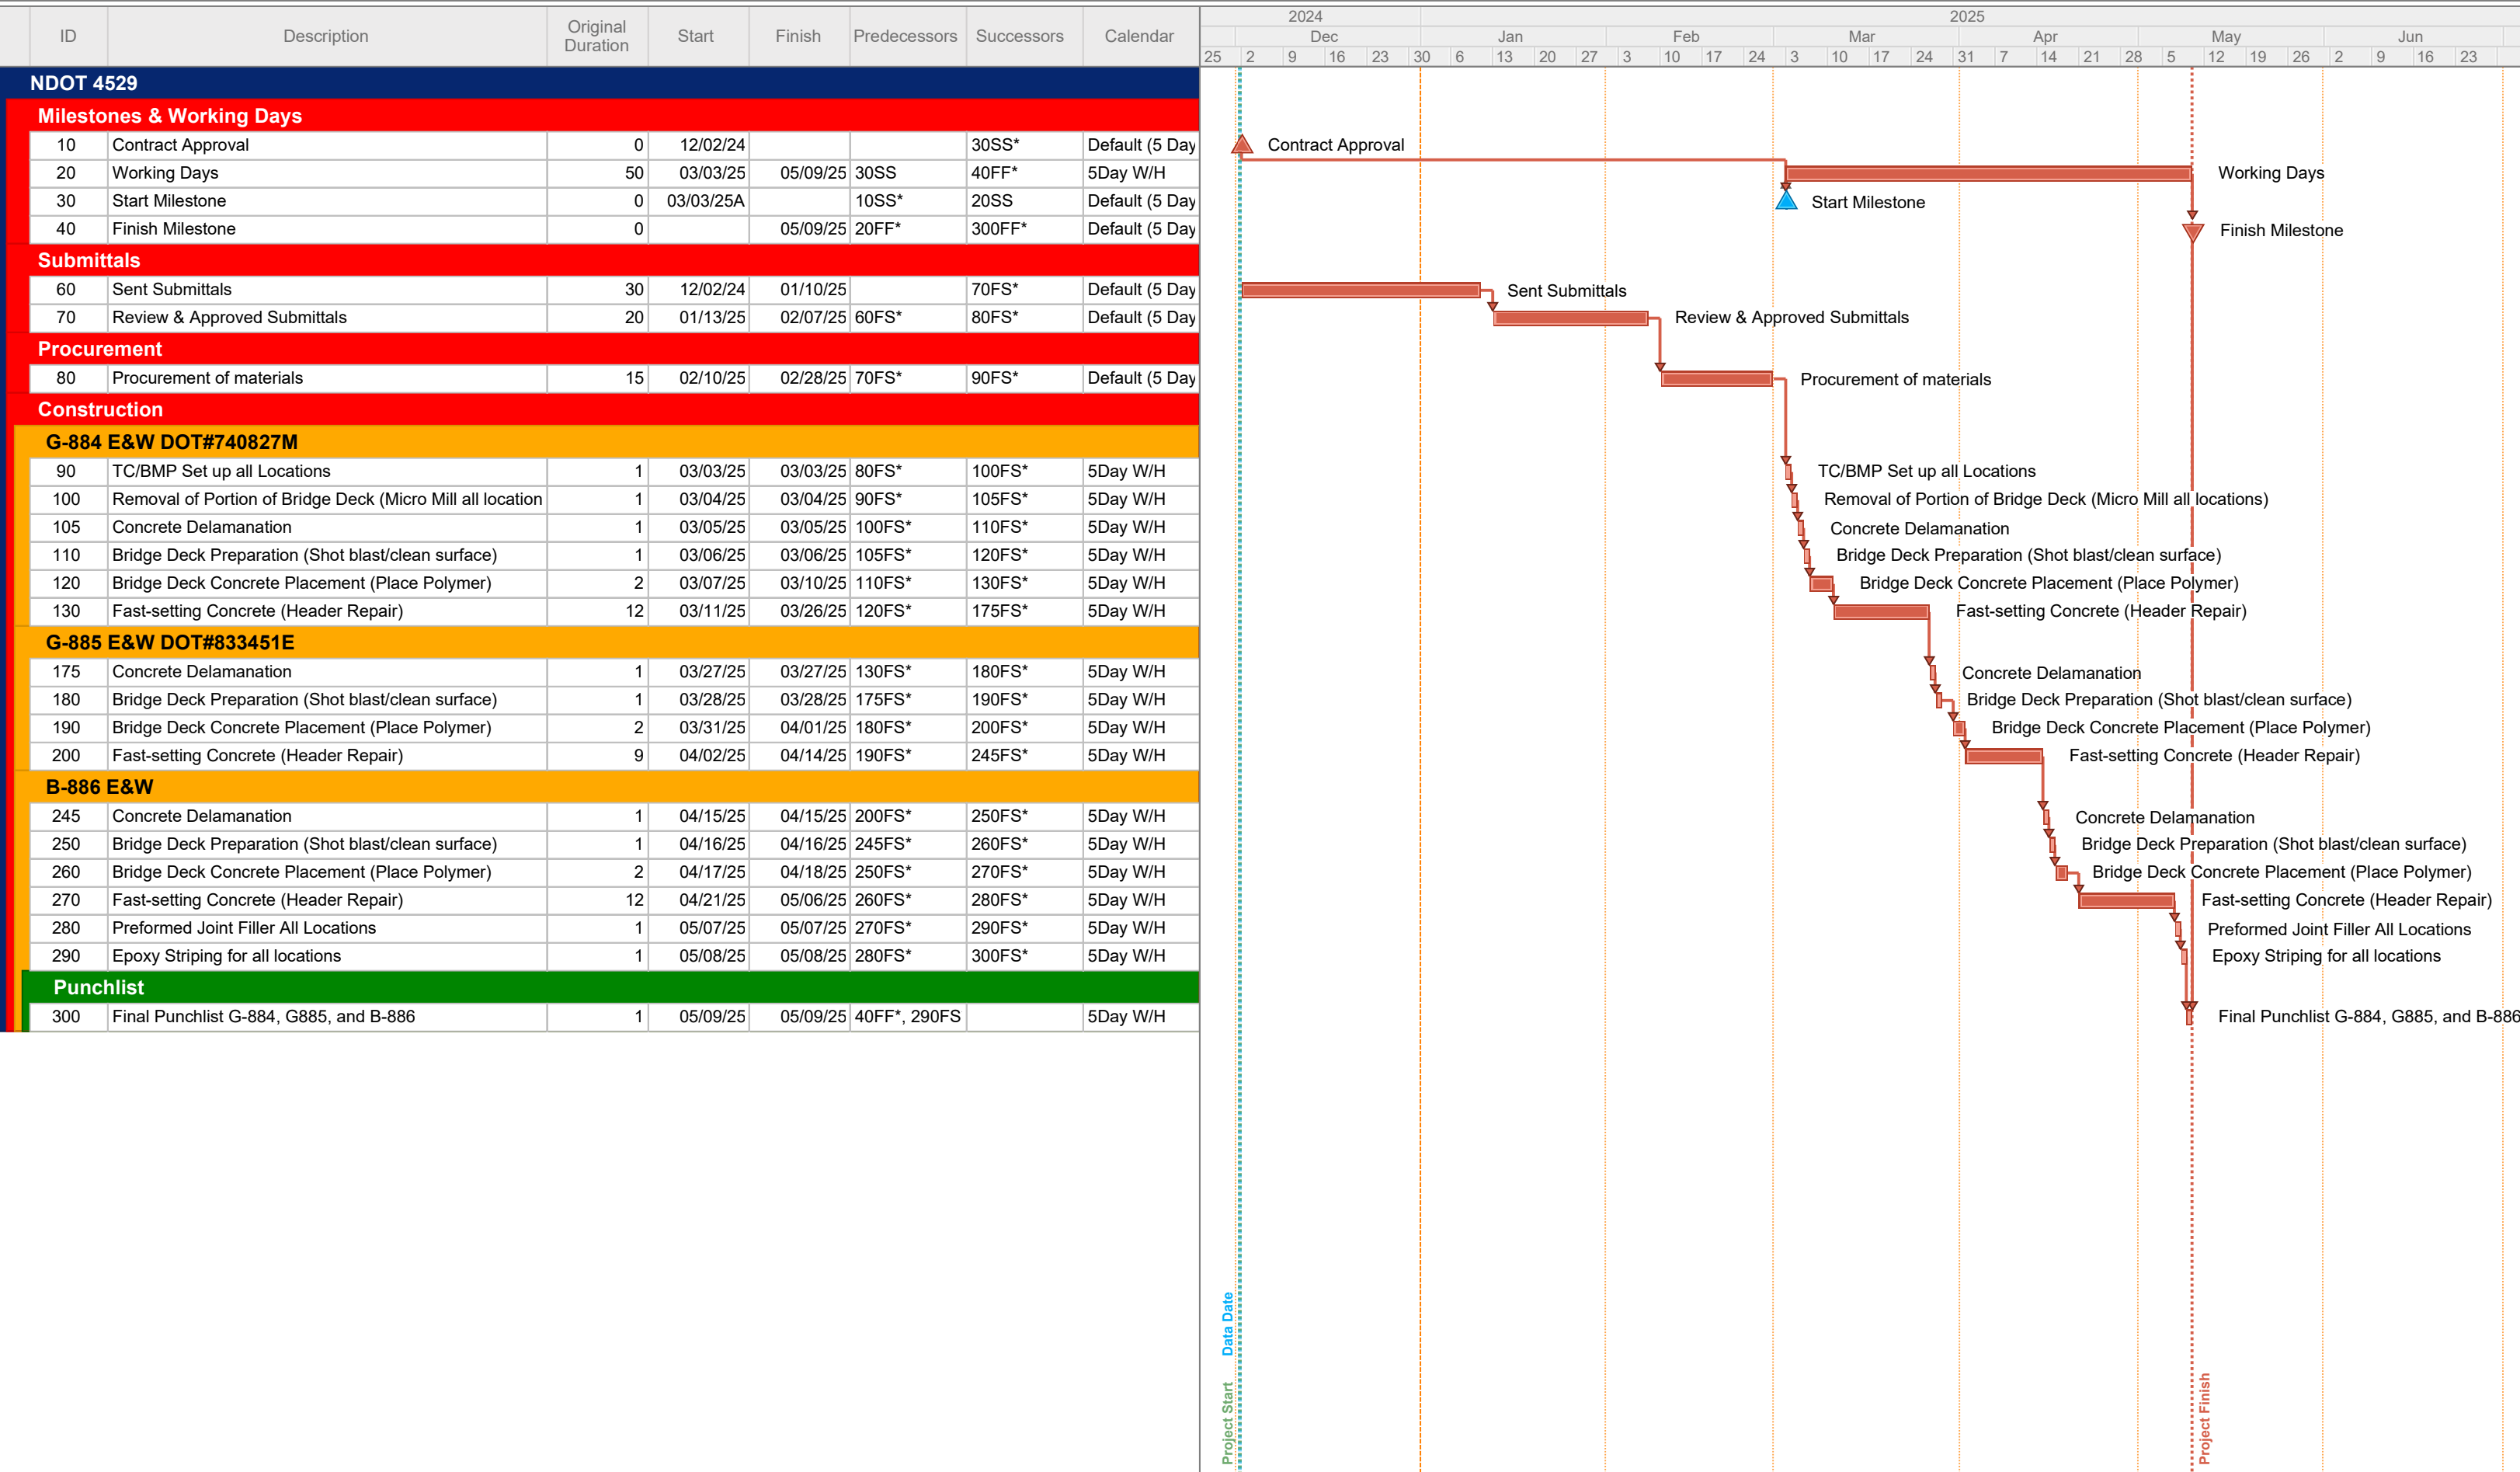

DEPARTMENT OF TRANSPORTATION

Construction Site Stormwater Inspection Form
For Water Pollution Control Managers

Report No.

Instructions: Conduct the inspection in the presence of the Department designated personnel and discuss your observations. Ask clarifying questions when needed. Provide a brief description of deficiencies in the appropriate "Comment Section." Utilize the "Additional Comments" section at the end of the document as necessary. Attach digital photographs of deficiencies or other noted issues of concern with the inspection form. Areas disturbed by construction activities that are not permanently stabilized and discharge into a receiving waterway or storm drain system shall have inspection priority. For projects that do not have a Resident Engineer, list the individual(s) responsible for construction administration.

Site Information

Project Location (Description from Contract Documents):

Contract Number:

Construction General Permit CSW/Tracking Number:

☐ N/A

NDOT Inspector and Crew Number:

Resident Engineer:

Contractor's Water Pollution Control Manager:

Date & Time of Inspection:

Date of Previous Inspection:

Site Conditions at the Time of Inspection

Weather Conditions:

☐ CLEAR☐ P. CLOUDY☐ OVERCAST☐ RAIN

Precipitation Intensity:

☐ NONE☐ LIGHT☐ MODERATE☐ HEAVY

Precipitation Reference (specify type and location):

Precipitation total identified from the precipitation event preceeding this inspection:

N/A

Wind:

☐ NONE☐ LIGHT☐ MODERATE☐ HEAVY

Temperature Range (°F)

☐ <32☐ 32-50☐ 51-75☐ >75

Is there a potential for construction stormwater runoff to discharge into an impaired or TMDL listed waterway? (See SWPPP)

☐ YES☐ NO

If yes, which waterway(s):

Were deficiencies identified during the previous inspection? If yes, describe the corrective action(s) implemented, or the steps taken in the non-compliance escalation process.

☐ N/A☐ YES☐ NO

Are there areas exhibiting significant erosion (rills, gullies, sheet erosion, etc.) as a result from construction activities?

☐ YES☐ NO

If yes, do any of these areas discharge into a waterway?

☐ N/A☐ YES☐ NO

If yes, which waterway(s) (if name is known)?

Is stormwater runoff being discharged onto the project area from adjacent areas?

☐ YES☐ NO

Are there any noticeable pollutant-related concerns regarding stormwater discharging from and/or onto the project area? If yes, briefly explain.

☐ YES☐ NO

SWPPP Elements

Is the SWPPP onsite & available?

☐ YES☐ NO

Is the SWPPP signed and certified?

☐ YES☐ NO

Is the SWPPP complete and up-to-date?

☐ YES☐ NO

Is the Construction General Permit information properly posted at the construction site?

☐ N/A☐ YES☐ NO

Best Management Practice (BMP) Categories

Sediment Control

Are sediment control measures required? If no, proceed to next sub-section.

☐ YES☐ NO

Are sediment control measures properly implemented?

☐ YES☐ NO

Comments:

Erosion Control

Are erosion control measures required? If no, proceed to next sub-section.

☐ YES☐ NO

Are erosion control measures properly implemented?

☐ YES☐ NO

Comments:

STATE OF NEVADA

DEPARTMENT OF TRANSPORTATION

Page 2 of 3

Construction Site Stormwater Inspection Form

For Water Pollution Control Managers

Track-Out Control		
Are track-out measures required? If no, proceed to next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		
Material Stockpiles		
Are there material stockpiles? If no, proceed to next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		
Concrete Washout		
Are concrete washout areas required? If no, proceed to next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		
Construction Material Storage		
Are construction materials stored onsite? If no, proceed to next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		
Chemical Storage		
Are chemicals, e.g. equipment fluids, paints, solvents, etc., stored onsite? If no, proceed to next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		
Fueling Areas		
Is there a temporary fueling area onsite? If no, proceed to next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		
Construction Equipment		
Is there evidence of equipment leaks and/or spills? If no, proceed to the next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		
Waste Material Storage		
Are waste materials stored onsite? If no, proceed to next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		
Sanitation Facilities		
Are portable toilets staged onsite? If no, proceed to next sub-section.	☐ YES	☐ NO
Are BMPs properly implemented?	☐ YES	☐ NO
Comments:		

DEPARTMENT OF TRANSPORTATION

Construction Site Stormwater Inspection Form

For Water Pollution Control Managers

Temporary Batch Plants			
Are there temporary batch plants associated with the project? If no, proceed to next sub-section.		☐ YES	☐ NO
Location of temporary batch plants?		☐ ONSITE	☐ OFFSITE
Are BMPs properly implemented?		☐ YES	☐ NO
Comments:			
Illicit Discharge Detection and Elimination / Spill Response			
Are there any illicit discharges? If yes, briefly describe the discharge in question.		☐ YES	☐ NO
Are there any spills meeting the reportable quantity threshold for the current inspection period? If yes, briefly describe the spill in question.		☐ YES	☐ NO
Was appropriate action taken to address the illicit discharge or spill?		☐ N/A	☐ YES ☐ NO
Was a spill report filed with NDEP?		☐ N/A	☐ YES ☐ NO
Was a non-reportable spill report completed during the inspection period? If yes, briefly describe the spill and actions taken.		☐ N/A	☐ YES ☐ NO
Have non-structural BMPs been implemented during the inspection period (i.e. Sweeping, drip pan, equipment diapers, etc.)? If yes, briefly describe.		☐ N/A	☐ YES ☐ NO
Final Check			
Were all non-stabilized and construction staging areas inspected? If no, provide a brief explanation.		☐ YES	☐ NO
Additional Comments Section			
Inspector _____		Date _____	
Reviewed By:			
Water Pollution Control Manager _____		Date _____	
I certify under penalty of law, that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations. [40 CFR 122.22(d)]			
